SE Lab 2 - Agile Backlog Creation & Sprint Simulation in Jira

Lakshya Budhauliya - Section C - 31 October 2026
Jira workspace: lakshyabudhauliya.atlassian.net - Project: SE LAB (key SCRUM)

1. Product backlog - Epics

The backlog for the Lab 1 telemedicine scenario (Telemedicine Slot Booking & Prescription Portal) is organized under four epics:

- SCRUM-5 Doctor Search & Consultation Booking
- SCRUM-6 Video Consultation & Notifications
- SCRUM-7 Prescription Management
- SCRUM-8 Authentication & Security

2. User stories, priorities and story point estimates

Key	Story	Epic	Priority	Pts	Sprint
SCRUM-14	Login with role-based authentication	Authentication & Security	High	3	1
SCRUM-9	Search and Filter Doctors	Doctor Search & Consultation Booking	High	5	1
SCRUM-16	Book a video consultation slot	Doctor Search & Consultation Booking	High	8	1
SCRUM-17	Booking confirmation with encrypted video room link	Video Consultation & Notifications	High	5	1
SCRUM-15	Reschedule or cancel a booking	Doctor Search & Consultation Booking	Medium	3	2
SCRUM-18	Join the encrypted video consultation	Video Consultation & Notifications	High	8	2
SCRUM-19	Request in-session technical support	Video Consultation & Notifications	Low	2	2
SCRUM-20	Author and digitally sign a prescription	Prescription Management	High	8	2
SCRUM-21	Validate doctor license before signing	Prescription Management	High	3	2
SCRUM-22	Download signed prescription PDF	Prescription Management	Medium	3	2
Total				**48**	

3. Sprint plan and execution

Sprint 1 (SCRUM Sprint 1): 31 October - 7 November 2026, 1 week. Scope: account access and booking flow - 4 stories, 21 story points. Goal: "Simulated - SE Lab 2 practice exercise". All 4 stories moved To Do -> In Progress -> Done and the sprint was completed.

Sprint 2 (SCRUM Sprint 2): 31 October - 7 November 2026, 1 week. Scope: consultation, support and prescription flow - 6 stories, 27 story points. Goal: "Simulated - SE Lab 2 practice exercise". All 6 stories moved To Do -> In Progress -> Done and the sprint was completed.

4. Evidence screenshots

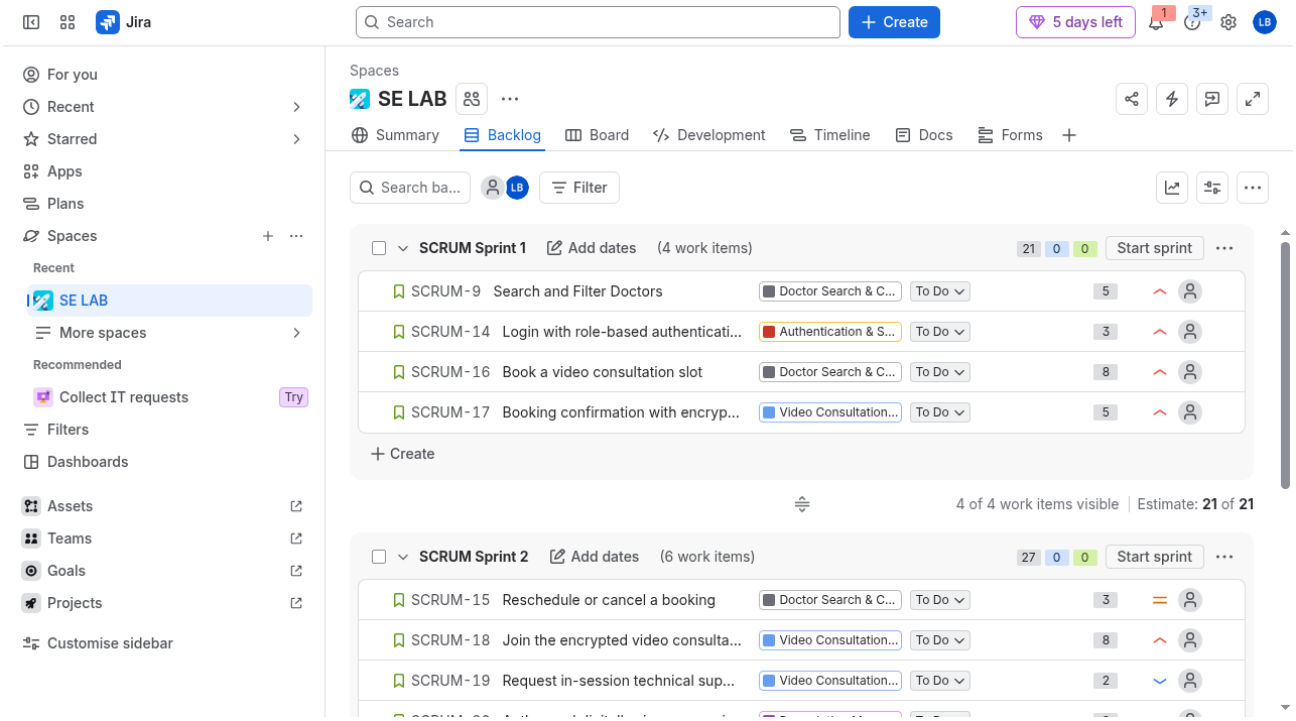


Fig 1 - Backlog organized into Sprint 1 and Sprint 2, with epic labels and story point estimates on each story.

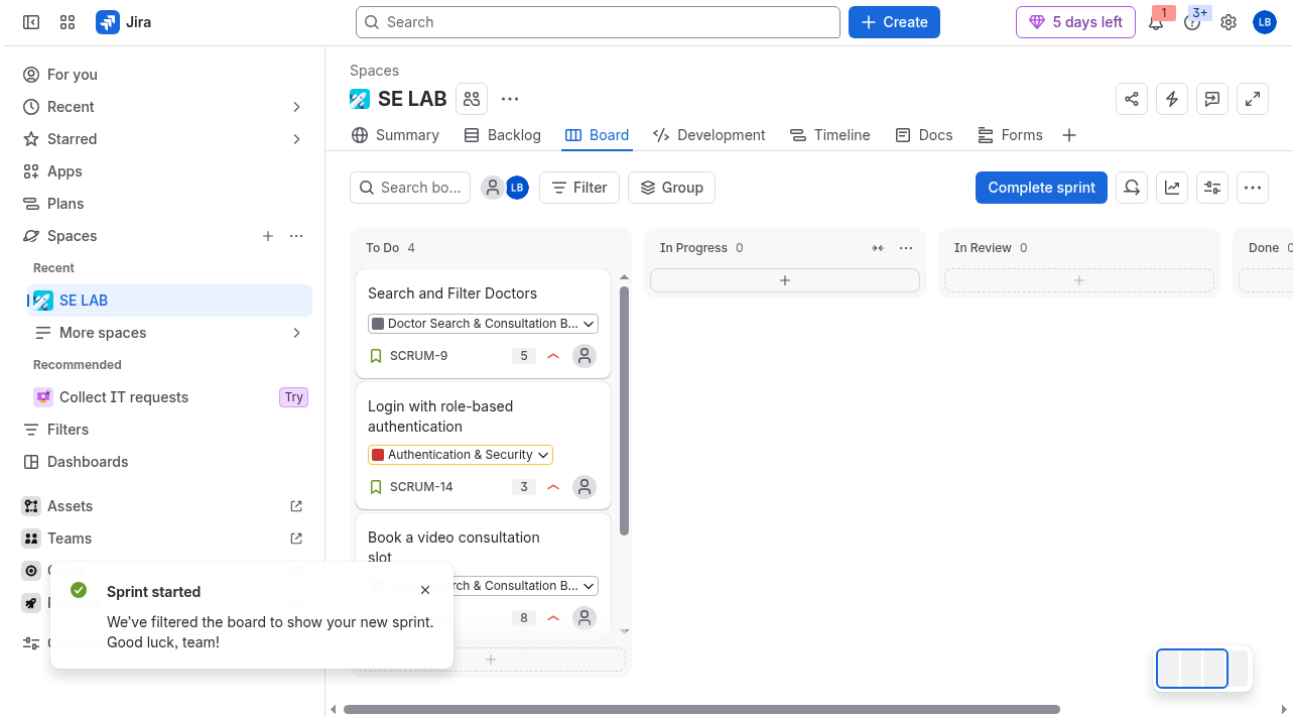


Fig 2 - Active Sprint 1 board at start: 4 stories (21 points) in To Do.

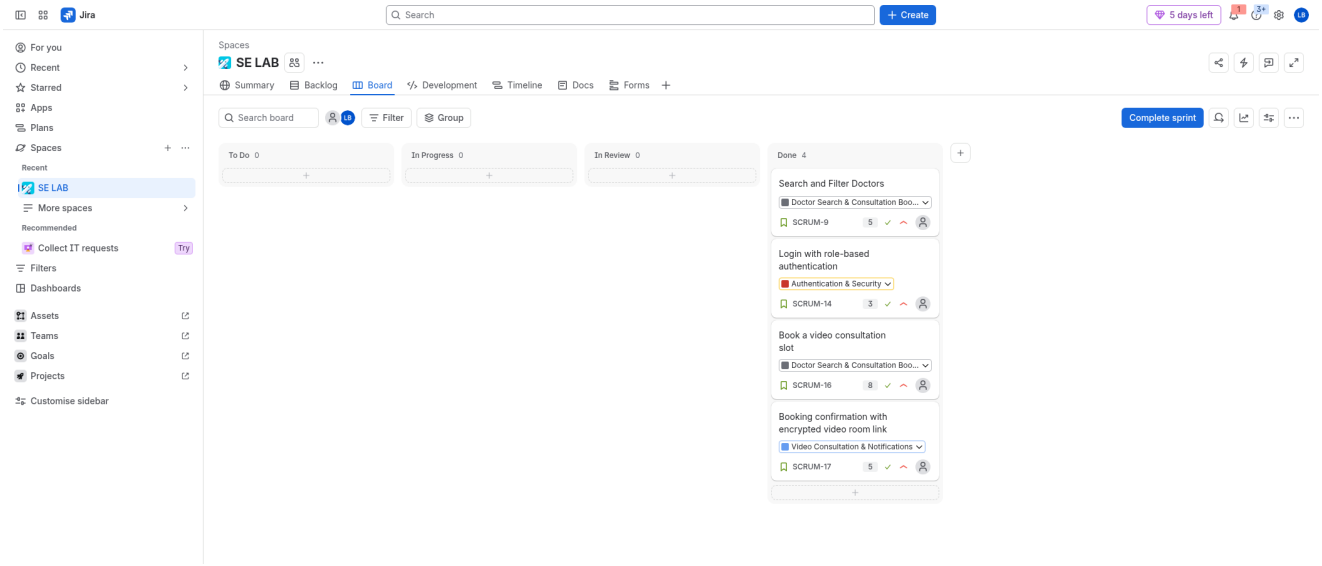


Fig 3 - Sprint 1 board after simulation: all 4 stories in Done.

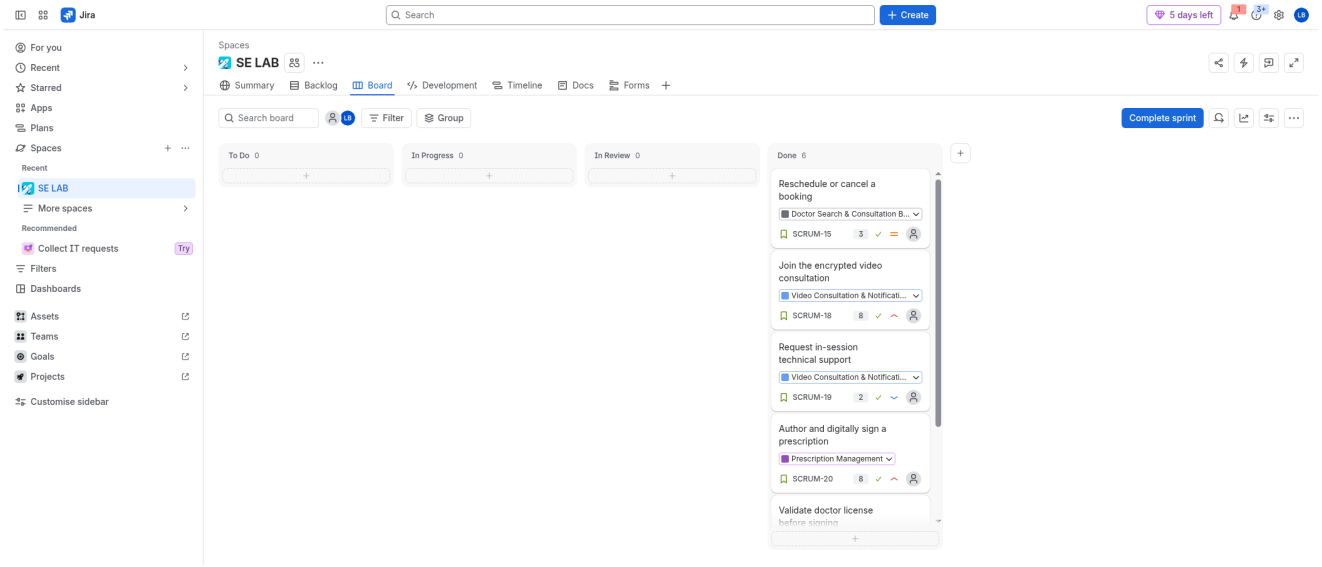


Fig 4 - Sprint 2 board after simulation: all 6 stories in Done.

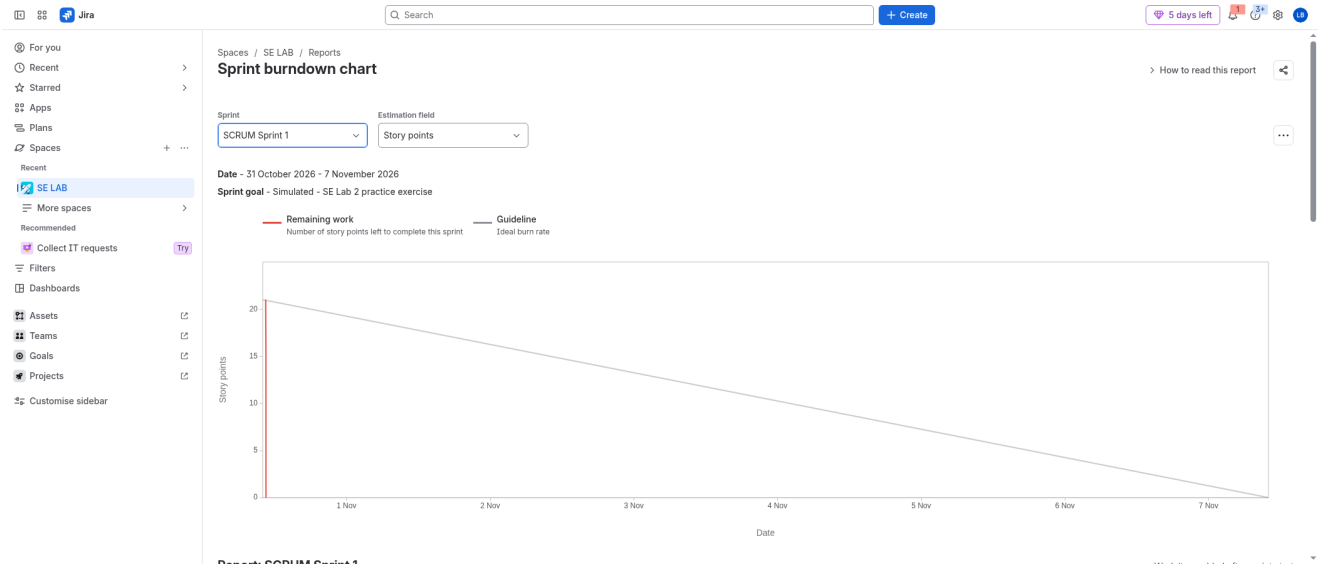


Fig 5 - Sprint 1 burndown chart (21 story points).

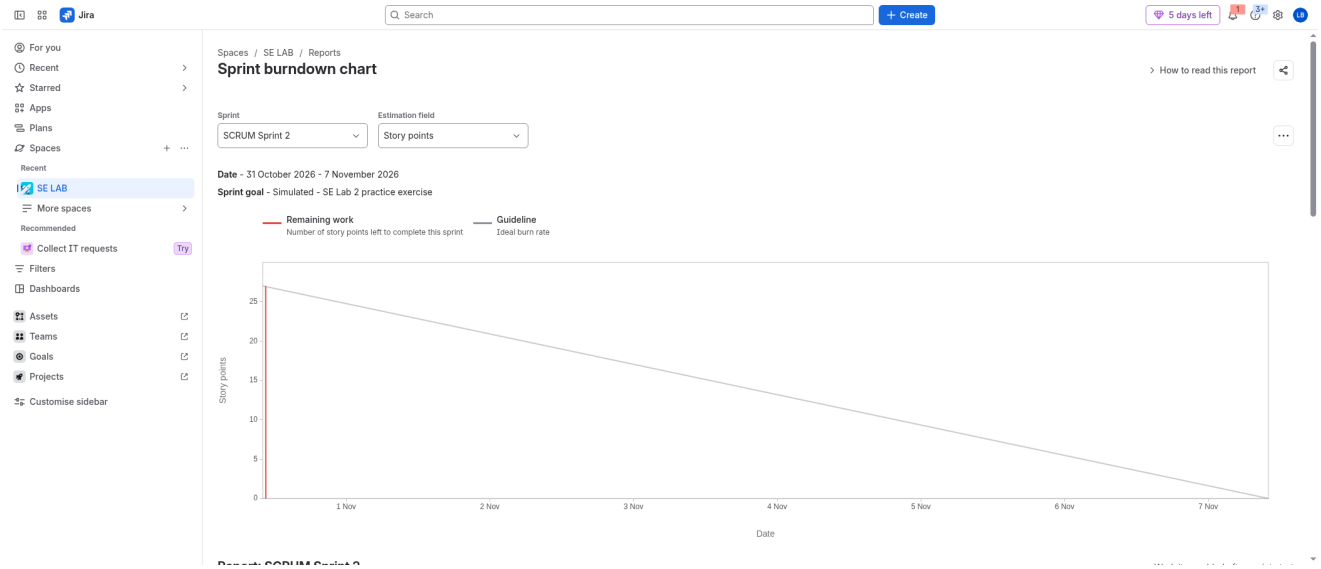


Fig 6 - Sprint 2 burndown chart (27 story points).

5. Reflection questions

1. How did your story point estimations compare to the actual effort during the sprint?

Honestly, I can't really compare them to actual effort here. I moved all the cards in one sitting, so nothing was actually built and no real effort got measured. The points mostly show how I sized the stories against each other. The riskier ones like booking a slot, joining the encrypted consultation and signing a prescription got 8 points, normal features got 3-5, and the small support item got 2. Whether those numbers are right is something only a real sprint with actual implementation work could show.

2. How did you decide the priority order of the backlog?

Priorities were set by user value and dependency. Stories the portal cannot function without - login, doctor search, booking, and joining the consultation - are High. Prescription authoring and doctor license validation are also High because they carry clinical and legal weight. Follow-on conveniences like rescheduling or cancelling a booking and downloading the prescription PDF are Medium, and in-session technical support is Low since it is a fallback rather than a core flow.

3. How did the sprint outcome compare to the sprint plan?

Both sprints delivered their full committed scope: Sprint 1 finished all 4 stories (21 points) and Sprint 2 all 6 stories (27 points), with no scope changes mid-sprint. Because execution was simulated, this shows the plan was coherent and the scope was logically split across the two sprints; it does not demonstrate delivery predictability the way completing real work within the sprint window would.

4. What insights does the burndown chart give about team capacity?

Limited ones in this exercise. Both charts show the entire scope burning down on day one because all card movements happened in a single session, so they say nothing about a team's real pace or capacity. What they do illustrate is how a burndown chart reads - committed scope against remaining work over time - and what to look for in a real sprint: a gradual daily burn that tracks the ideal line, with flat sections or spikes flagging blockers or added scope.
